PROJECT MANAGEMENT DOCS

Free Project Management Templates

PROJECT MANAGEMENT PLAN TEMPLATE

This Project Management Plan Template is free for you to copy and use on your project and within your organization. We hope that you find this template useful and welcome your comments. Public distribution of this document is only permitted from the Project Management Docs official website at:
www.ProjectManagementDocs.com

PROJECT MANAGEMENT PLAN

HEALTH TRACKER

COMPANY NAME
STREET ADDRESS
CITY, STATE ZIP CODE

Table of Contents

INTRODUCTION 2
PROJECT MANAGEMENT APPROACH 2
PROJECT SCOPE 3
MILESTONE LIST 3
SCHEDULE BASELINE AND WORK BREAKDOWN STRUCTURE 4
CHANGE MANAGEMENT PLAN 4
COMMUNICATIONS MANAGEMENT PLAN 5
COST MANAGEMENT PLAN 7
PROCUREMENT MANAGEMENT PLAN 9
PROJECT SCOPE MANAGEMENT PLAN 9
SCHEDULE MANAGEMENT PLAN 10
QUALITY MANAGEMENT PLAN 11
RISK MANAGEMENT PLAN 13
RISK REGISTER 13
STAFFING MANAGEMENT PLAN 13
RESOURCE CALENDAR 15
COST BASELINE 15
QUALITY BASELINE 16
SPONSOR ACCEPTANCE 17

Introduction

The **Health Tracker (TRACKER)** project is a mobile application for the Android OS developed by a team of five students. The product is designed to combat bad habits through gamification, social support, and AI-driven relapse risk prediction. While existing solutions on the market act reactively by simply recording relapses, **TRACKER** aims to be a proactive tool. It analyzes the user's current state—such as stress levels and behavioral patterns—to warn of a high probability of relapse before it occurs, providing psychological support and preventive recommendations "here and now".

Project Management Approach

The Project Manager, **Cherepanov**, has the overall authority and responsibility for managing and executing this project according to this Project Plan and its Subsidiary Management Plans. The project team consists of five specialists:

- **Project Manager (Cherepanov):** Team management, deadline control, and documentation.
- **Technical Steward (Voloshyn):** Server architecture, REST API, and cloud technologies.
- **Lead Developer (Chepel):** Android client-side development and app logic.
- **UI/UX Designer (Semenyuk):** Interface design, Figma mockups, and frontend layout.
- **Data Analyst (Tsvetkov):** ML model development for prediction and data analytics.

All project plans and funding decisions are reviewed and approved by the Project Sponsor, **Dorosh**. The team follows an Agile methodology to ensure flexibility during the development of the AI module and social features.

Project Scope

The scope of the **Health Tracker** project includes the planning, design, development, and testing of a native Android application. Key components include:

- **Mobile App (MVP):** A functional Android application with a Dark Mode interface, retention timer, and progress calendar.
- **AI Prediction Module:** A machine learning algorithm (Python/Scikit-learn) to analyze user behavior patterns.
- **Backend Server:** A secure cloud-based REST API (FastAPI) for data synchronization.
- **Social Features:** An anonymous community feed for mutual support and a gamification system.

The project is considered complete when the final APK file is generated, the server is deployed with Swagger documentation, and the full source code is uploaded to GitHub.

Milestone List

The table below lists the major executive milestones for the **Health Tracker** project based on the 2026 development schedule.

Milestone	Description	Date
Project Initiation	Approval of the project theme, team formation, and Charter finalization.	**March 13, 2026**
Design & Database Prototype	Completion of Figma UI mockups and ER database schema.	**March 20, 2026**

Milestone	Description	Date
MVP Development (Alpha)	Realization of core timer logic, user login, and basic API connectivity.	**April 08, 2026**
Feature Complete (Beta)	Integration of the AI prediction module and anonymous social feed.	**April 14, 2026**
Final Release & Defense	Completion of QA testing, final APK assembly, and project defense.	**April 24, 2026**

ОСЬ ГОТОВИЙ ТЕКСТ ДЛЯ РОЗДІЛУ **SCHEDULE BASELINE AND WORK BREAKDOWN STRUCTURE**. Я АДАПТУВАВ ЙОГО ПІД ТВІЙ ПРОЕКТ **HEALTH TRACKER**, ЗМІНИВ НАЗВИ ТА ВКАЗАВ ТВОГО МЕНЕДЖЕРА ПРОЕКТУ.

Schedule Baseline and Work Breakdown Structure

This section discusses the Work Breakdown Structure (WBS), WBS Dictionary, and Schedule Baseline, and how they are used to manage the **Health Tracker** project's scope. The WBS provides the work packages to be performed for the completion of the project. The WBS Dictionary defines these work packages in detail. The schedule baseline provides a reference point for managing project progress as it pertains to the schedule and timeline. The schedule baseline and WBS were created using **GanttPRO** software to ensure clear visualization of task dependencies and resource allocation.

The WBS for the **Health Tracker** Project is comprised of work packages that do not exceed 40 hours of work but are at least 4 hours of work. These work packages were developed through close collaboration among project team members, including the Technical Steward, Lead Developer, and UI/UX Designer, to ensure all technical requirements of the Android application and AI module are covered.

The WBS Dictionary defines all work packages for the **Health Tracker** Project. These definitions include all tasks, resources (such as **Cherepanov** for Backend and **Chepel** for Android), and deliverables (such as the ER Diagram and API documentation). Every work package in the WBS is defined in the WBS Dictionary and aids in resource planning, task completion, and ensuring deliverables meet project requirements.

The **Health Tracker** Project schedule was derived from the WBS and Project Charter. The schedule was completed, reviewed by the Project Sponsor (**Dorosh**), and approved as the baseline. The schedule is maintained as a **Gantt Chart** by the Project Manager, **Voloshyn**. Any proposed changes to the schedule will follow the project's change control process. If established boundary controls are exceeded, a change request will be submitted to the Project Manager. The Project Manager and team will determine the impact of the change on the schedule, cost, resources, scope, and risks. If it is determined that the impacts exceed the boundary conditions, the change will be forwarded to the Project Sponsor for review and approval.

The **Health Tracker** boundary conditions are:

- **CPI** (Cost Performance Index) less than 0.8 or greater than 1.2.

- **SPI** (Schedule Performance Index) less than 0.8 or greater than 1.2.

If the change is approved by the Project Sponsor, it will be implemented by the Project Manager, who will update the schedule and all documentation and communicate the change to all stakeholders in accordance with the Change Control Process.
The Project Schedule Baseline and Work Breakdown Structure are provided in **Appendix A, Project Schedule** and **Appendix B, Work Breakdown Structure**.

CHANGE MANAGEMENT PLAN

This section describes the change control process for the **Health Tracker** project. Any changes must be carefully considered, and their impact on cost, risk, schedule, and scope must be clear before approval decisions are made. Oversight is provided by the **Change Control Board (CCB)**, which reviews, approves, or denies proposed changes.
The following steps comprise the organization's change control process for the **TRACKER** project:

- **Step #1: Identify the need for a change (Any Stakeholder)** – The requestor submits a completed change request form to the Project Manager.
- **Step #2: Log change in the register (Project Manager)** – **Voloshyn** maintains a log of all change requests throughout the project duration.
- **Step #3: Conduct evaluation (PM, Team, Requestor)** – **Voloshyn** evaluates the impact of the change on cost, risk, schedule, and scope.
- **Step #4: Submit request to CCB (Project Manager)** – **Voloshyn** submits the request and analysis to the CCB for review.
- **Step #5: CCB Decision** – The CCB discusses the proposal and decides on approval based on all submitted information.
- **Step #6: Implement change (Project Manager)** – If approved, **Voloshyn** updates project documentation and communicates changes to the team and stakeholders.

The **Project Sponsor (Dorosh)** chairs the CCB, and any changes to project scope, cost, or schedule must meet his approval.

Communications Management Plan

This plan defines the communication requirements and frameworks for the **Health Tracker** project. **Voloshyn** takes the lead role in ensuring effective communications.

Communications Matrix

Communication Type	Description	Frequency	Format	Participants	Owner
Weekly Status Report	Summary of project status.	Weekly	Email	Sponsor, Team	**Voloshyn**
Project Team Meeting	Review action register and status.	Weekly	In Person	Project Team	**Voloshyn**
Technical Design Review	Review of technical work or designs.	As Needed	In Person	Project Team	**Voloshyn**
Final Project Defense	Final presentation of the result.	Once	In Person	Sponsor, Team	**Voloshyn**

Project Team Directory

Name	Role	Email	Project Responsibilities
Dorosh	Project Sponsor	vitaliy.dorosh@gmail.com	Final project approval and evaluation.
Voloshyn	Project Manager	anonum345@gmail.com	Team management and deadline control.
Chepel	Lead Developer	chepel333@gmail.com	Android development and app logic.
Semenyuk	UI/UX Designer	grozniy324@gmail.com	Interface design and Figma mockups.
Tsvetkov	Data Analyst	tsvetkovartem333@gmail.com	ML model development and analytics.
Cherepanov	QA & Documentation	a.cherepanov333@gmail.com	Quality control and manual testing.

Communications Conduct

- **Meetings: Voloshyn** distributes an agenda at least 2 days prior to scheduled meetings. **Cherepanov** acts as the recorder for meeting notes.
- **Email:** All emails pertaining to the **TRACKER** project must be professional and include **Voloshyn** on all communications.
- **Informal Comms:** Any critical updates or concerns arising from informal discussions must be communicated to **Voloshyn** so appropriate action may be taken.

Ось готовий текст для розділів **Cost Management Plan** та **Procurement Management Plan**, повністю адаптований під твій проект **Health Tracker (TRACKER)**.

Cost Management Plan

The Cost Management Plan defines how costs for the **Health Tracker** project will be managed, reported, and controlled throughout its lifecycle. **Voloshyn (Project Manager)** is responsible for managing and reporting on all project costs. **Dorosh (Project Sponsor)** holds the final authority for all budget decisions and approval of changes.

Key management standards for the **TRACKER** project include:

- **Measurement and Reporting:** Cost performance is measured using earned value calculations. **Voloshyn** will present these metrics during monthly status meetings to identify any deviations from the budget.
- **Control Accounts:** Costs and performance are managed and tracked at the fourth level of the Work Breakdown Structure (WBS).
- **Credit Rules:** A "50/50" credit rule applies: work packages receive 50% credit when work starts and the remaining 50% upon total completion.
- **Performance Indexes:**
    - **Yellow Status (Cautionary):** A variance of 10% (+/- 0.1) in the Cost Performance Index (CPI) or Schedule Performance Index (SPI).
    - **Red Status (Critical):** A variance of 20% (+/- 0.2) in CPI or SPI. This requires immediate corrective action from **Voloshyn** and approval from the Change Control Board (CCB).

If calculations indicate that values are approaching the critical stage, **Voloshyn** must communicate this to **Dorosh** immediately.

Procurement Management Plan

The Procurement Management Plan identifies the steps and responsibilities for any external purchases required for the **Health Tracker** project. **Voloshyn** provides oversight and management for all procurement activities.

- **Approval Authority: Voloshyn** is authorized to approve procurement actions up to **$50,000**. Any actions exceeding this amount require approval from **Dorosh**.
- **Procurement Process:** While this project expects minimal or no procurement, any necessary items or services will be identified by the project team. **Voloshyn** ensures these are presented to the appropriate purchasing groups to determine if it is more advantageous to build or buy the required resource.
- **Vendor Management:** In the event a vendor is selected, **Voloshyn** is responsible for managing the external resource and measuring their performance regarding the delivery of goods or services.

ОСЬ ГОТОВІ ТЕКСТИ ДЛЯ НАСТУПНИХ РОЗДІЛІВ ТВОГО **PROJECT MANAGEMENT PLAN**. Я АДАПТУВАВ ЇХ ПІД ТВІЙ ПРОЕКТ **HEALTH TRACKER (TRACKER)**, ВРАХУВАВ ЗМІНУ РОЛЕЙ (ТИ — МЕНЕДЖЕР ПРОЕКТУ) ТА ДОДАВ СПЕЦИФІЧНІ РИЗИКИ З ТВОГО СТАТУТУ.

Project Scope Management Plan

Scope management for the **Health Tracker** project is the responsibility of the Project Manager, **Voloshyn**. The scope is defined by the Scope Statement, Work Breakdown Structure (WBS), and WBS Dictionary. **Voloshyn**, along with the Project Sponsor (**Dorosh**) and stakeholders, approves documentation for measuring scope, including deliverable quality checklists. Proposed scope changes may be initiated by any team member. All requests are submitted to **Voloshyn**, who evaluates the impact. If accepted, the request moves to the Change Control Board (CCB) and **Dorosh** for final approval. **Dorosh** is responsible for formally accepting the final project deliverables based on a review of documentation, AI model accuracy, and app functionality.

Schedule Management Plan

Project schedules for the **TRACKER** project are created using **GanttPRO**, starting with deliverables identified in the WBS. Activity definition identifies specific work packages, such as "AI Data Collection" or "Android Layouts".

Milestones for the project schedule include:

- **Project Initiation & Charter Approval** — March 13, 2026.
- **Design & Database Prototype Completion** — March 20, 2026.

- **MVP Development (Alpha Version)** — April 08, 2026.
- **Feature Completion (Beta Version)** — April 14, 2026.
- **Final Project Defense** — April 24, 2026.

Voloshyn facilitates work package definition and maintains the schedule. The project team (including **Chepel** and **Semenyuk**) participates in duration estimating and validates the proposed schedule before it is baselined by **Dorosh**.

Quality Management Plan

Quality management ensures that the **Health Tracker** deliverables, such as the **app-release.apk** and **REST API**, meet established standards.

- **Dorosh (Sponsor):** Approves quality standards and signs off on final acceptance.
- **Voloshyn (PM):** Implements the Quality Management Plan and ensures all processes are compliant.
- **Cherepanov (QA & Documentation):** Maintains Quality Control logs and performs manual testing to find bugs.
- **Lead Developer (Chepel):** Ensures code quality and adheres to the technical requirements, such as API latency under **500ms**.

Risk Management Plan

The approach for managing risks for the **TRACKER** project involves identifying and ranking risks to implement mitigation strategies proactively. Key identified risks include:

- **Loss of Server Connection:** Mitigated by implementing an "Offline-first" architecture using a local **Room** database.
- **Lack of Experience with Kotlin:** Mitigated by conducting internal **Code Reviews** and pair programming sessions.

Voloshyn analyzes each risk during the project closing process to identify improvements for future projects, which are captured in the lessons learned knowledge base.

Ось готові тексти для розділів **Risk Register**, **Staffing Management Plan** та **Resource Calendar**, адаптовані під твій проект **Health Tracker (TRACKER)**.

Risk Register

The Risk Register for the **TRACKER** project is provided in **Appendix C, Risk Register**. It includes a methodical ranking of identified risks, such as the potential loss of server connection and the team's initial lack of experience with Kotlin. Each entry includes a corresponding mitigation strategy, such as implementing an offline-first architecture with a local **Room** database to ensure continuous app functionality.

Staffing Management Plan

The **Health Tracker** project utilizes a matrix organizational structure, where all development and management work is performed internally by the student team.

The staffing requirements and key roles are as follows:

- **Project Manager (Voloshyn):** Responsible for overall project management, planning work activities, tracking variances, reporting status to the sponsor, and coordinating team efforts.
- **Lead Developer (Chepel):** Responsible for the Android client-side development, core application logic, and managing network interactions.
- **UI/UX Designer (Semenyuk):** Responsible for interface design, creating high-fidelity mockups in Figma, and frontend layout/styling.
- **Data Analyst (Tsvetkov):** Responsible for data preparation, analytics, and the development of the machine learning model for relapse prediction.
- **QA & Documentation (Cherepanov):** Responsible for quality control, manual testing, managing project documentation, and monitoring internal deadlines.

Resources are allocated internally, and all project roles have been approved by the Project Sponsor, **Dorosh**.

Resource Calendar

The **Health Tracker** project requires the active participation of all team members for the entire duration of the project, from **March 9, 2026**, to **April 24, 2026**.

While all members are involved throughout the lifecycle, the level of effort varies based on the project phase:

- **Initial Phase:** High effort from the PM and Designer for requirements and Figma mockups.
- **Development Phase:** Peak effort from the Lead Developer, Data Analyst, and PM for API and MVP creation.
- **Testing Phase:** Focused effort from the QA specialist and the entire team for bug fixing and final assembly.

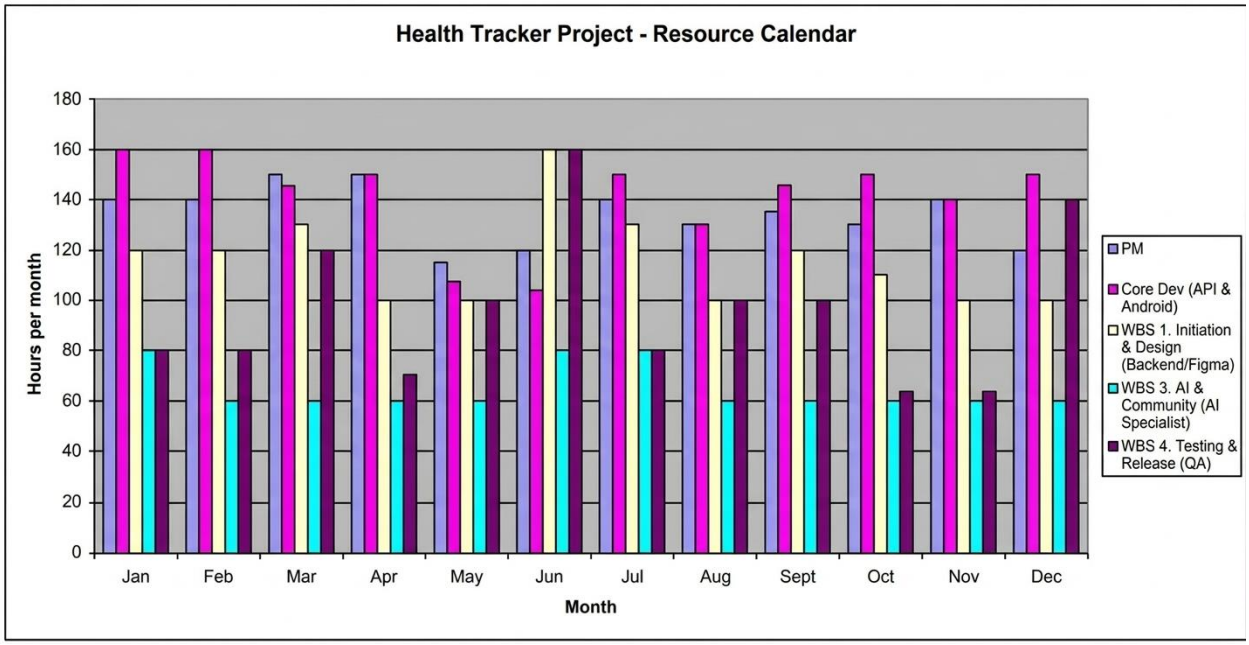

Ось адаптовані розділи **Cost Baseline** (Базовий план витрат) та **Quality Baseline** (Базовий план якості) для твого проекту **Health Tracker**.
Я зберіг структуру, але змінив зміст під специфіку мобільного додатка з AI-функціями.

Cost Baseline

Цей розділ містить базовий план витрат проекту, на основі якого здійснюватиметься управління бюджетом. Для відстеження витрат використовуватимуться метрики освоєного обсягу (Earned Value). Базовий план є основою для звітності та контролю фінансів.
Базовий план витрат проекту **Health Tracker** включає всі закладені кошти, необхідні для успішного завершення розробки MVP.

Фаза проекту	**Бюджет (Total)**	**Коментарі**
Planning & Design	$5,000	Робота над статутом, проектування бази даних (ER-діаграми) та створення UI/UX макетів у Figma.
Core Development	$15,000	Розробка серверної частини (API), верстка Android-екранів та логіка таймерів активності.
AI & Community	$10,000	Збір даних, тренування AI-моделей для рекомендацій та розробка логіки стрічки спільноти.
Testing & QA	$5,000	Пошук багів, тестування точності алгоритмів та підготовка фінальної

Фаза проекту	Бюджет (Total)	Коментарі
		збірки APK.
Deployment & Closeout	$3,000	Реліз у стори, передача документації та формальне закриття проекту.

Quality Baseline

Цей розділ визначає стандарти якості, яким має відповідати **Health Tracker**. Базовий план якості слугує основою для вимірювання успішності проекту. Програмне забезпечення має відповідати або перевищувати ці показники.

Показник (Item)	Допустимий рівень	Коментарі
Точність AI-трекера	Мінімум 95% точності	Коректність розпізнавання активності або підрахунку калорій на основі вхідних даних.
Швидкість API	< 300 мс на запит	Час відповіді сервера при завантаженні стрічки або збереженні тренування.
Стабільність (Crash-free)	99% сесій без помилок	Відсутність критичних збоїв програми на Android-пристроях під час тестування.
UI Responsiveness	Без затримок інтерфейсу	Плавність анімацій та відсутність "зависань" при переході між екранами.

Sponsor Acceptance

Approved by the Project Sponsor:

Date: <Sponsor Name>
<Sponsor Title>
